

MAIL TO:
 WATER SUPPLY BRANCH
 DIVISION OF WATER RESOURCES
 P.O. BOX 1401
 DOVER, DELAWARE 19903

STATE OF DELAWARE
 DEPARTMENT OF NATURAL RESOURCES
 AND ENVIRONMENTAL CONTROL

WELL COMPLETION REPORT MUST
 BE RETURNED 30 DAYS AFTER
 CONSTRUCTION DATE

MONITOR WELL COMPLETION REPORT

PH 42-05

PLEASE PRINT OR TYPE

PERMIT NO. 79005 LOCAL ID MWD
 Owner DEL. GEOL. SURVEY
 Address UNIV. OF DELAWARE
 City NEWARK State DE Zip 19714
 Telephone Number 451-2833
 Consulting Firm/Supervising Geologist (If applicable)
DGS/A.S. ANDRES
 Telephone Number 451-2847
 Well Contractor DGS
 Date of Completion 6-20-89
 Drilling Method: AUGER

WELL CONSTRUCTION

Total depth drilled: 184
 Depth to water 11.08
 Surveyed Top of Casing Elevations
 Inner _____ Outer _____ Ft. above Sea Level

CASING SEQUENCE	
Inner casing	Outer casing
5	0
40	5
2	2
PVC	GALV. STEEL

SCREEN SEQUENCE	
Inner casing	Outer casing
40	
45	
2	
PVC	


Type of Grout BENT. from 1 to 16
 Gravel pack interval from NONE to _____
 Aquifer/Formation screened in: COLUMBIA

Samples Logged By: A.S. ANDRES
 (Name)

HYDROGEOLOGIST D.G.S.
 (Title) (Company)

Well Drilled By: D.G.S.
 (Company Name)
Richard E. Brando 6/23/89
 (Signature of Driller in Charge) (Date)

IS COMPLETED WELL LOCATED AS SHOWN ON APPLICATION FORM? YES [] NO []
 IF NO, DESCRIBE LOCATION CHANGE OR OTHER COMMENTS.

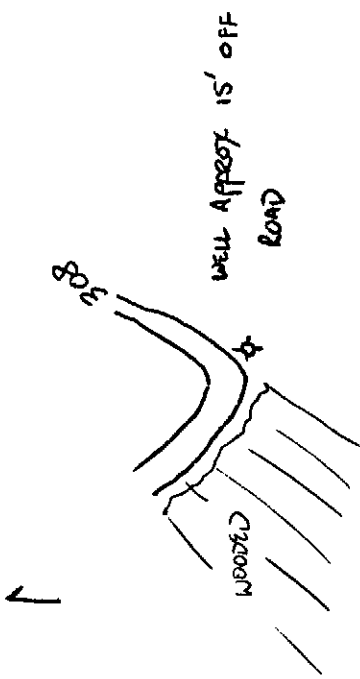

DRILLERS LOG DESCRIP.	TOP OF STRATA	BOTTOM
FILL - SAND, f, Silty + f. Gravel	0	1
TOPSOIL - SILT/CLAY Sandy	1	2
SILT/CLAY Sandy f-m Red Brn	2	5.5
SAND f-m, tr Silt, fine brown	5.5	8.5
SAND m-c, yellow-gray	8.5	13
SAND m-m, tr Gravel, f yellow-gray, interbedded with SAND m-c and SAND f-m tr Silt	8.5 13	
SAND f-m, Silty	64	64
SAND c, gray-yellow		66
GRAVEL f-m Sandy c	66	90
SAND c, Gravelly f-m	90	91
SILT, Sandy, Clayey	91	96
green-gray	96	104

SUPPLEMENTAL DRILLERS LOG ATTACHED?
 YES [] NO [] **GAMMA LOG AVAILABLE**
 PAGE 1 OF _____ PAGES **AT D.G.S.**
