


Log # 84 W # 802 County Shenandoah - 200 Date 3/8/63
 Owner A. L. Lecraw (W.L. Myers, Inc.) Use Domestic
 Location 2.5 mi. S.W. of Macanie, on NW side of 611
1.5 mi. SSW of Jct. of 611 and 263

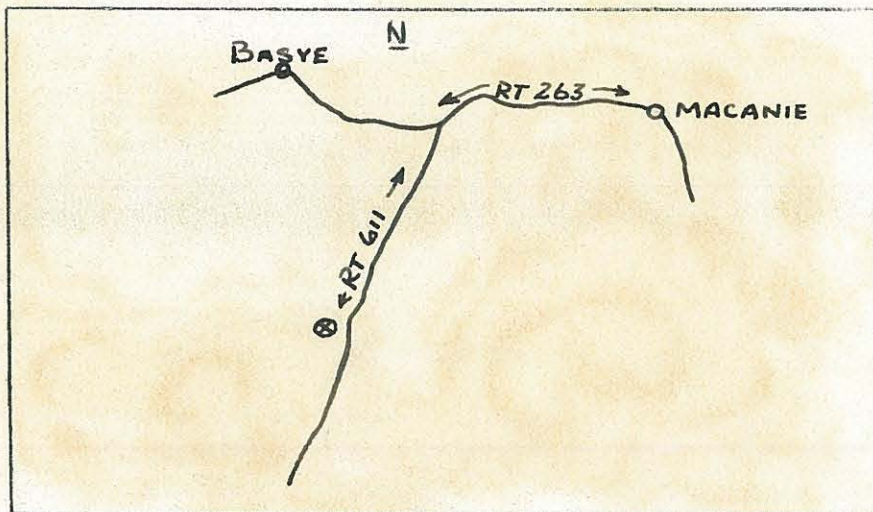

Well Data

Driller: Sydnor Pump & Well Co.
 Completed: 3/6/63
 Total Depth: 500' (Driller)
 Static W. L.: 125 (Tape)
 Casing: 5" x 102½'
 Bedrock: 26 (Driller)
 Hole Size: 8 3/4" x 102', 5" x 398'
 Yield: 7 gpm
 H₂O Temp: -
 Aquifers: Small seams at approx.
288, 322, 360, 408, 500 (Driller)
 Elev: 1745' (Topo)
 Geology: Chemung frm.

Instrument Data

↑ SP setting 10 Mv Approx. 52' /min.
 ↓ Res. " 200 Ohm-m " 40' /min.
 ↑ Gamma " .01 Mr " 25' /min.
 T. C. " E3, G10
 Fluid: Fresh Water
 Running Time 1 Hrs. 30 Mins.
 Depth of Log: Elec. 498' Gamma 498'
 Ground Electrode in mud pit 5' from well

Remarks Left curve dead - SP and Gamma on reverse.

Logged By DeKay and Whitfield
