66774

Water Well Contrac

P831-04

WATER SUP

CUSTOMER John Thomas JOB 879

ADDRESS 1164 Airport Rd. Seaford, Dela. DATE 10/1

LOCATION Horseshoe Development

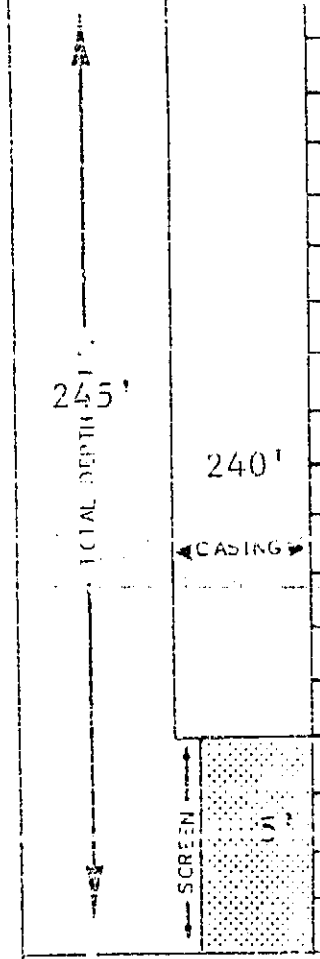

FEET FROM GROUND SURFACE 0 TO.....	WELL LOG
0-1	Topsoil
1-5	Clay sand
5-20	Fine med. sand
20-30	Fine coarse white sand
30-61	Gravel clay
61-125	Fine med. sand brown
125-160	Fine clay sand
160-190	Clay
190-230	Clay shell
230-240	Fine sand
240-261	Fine med. gray sand
261-275	Fine med. gray sand w/2% clay
275-280	Clay

WELL NO. 1	DIAMETER OF WELL 6"	DEPT. OF WELL 245'
HRS. PUMPED 4	SLOT SIZE .032	TYPE OF CASING PVC
CAPACITY G.P.M. 180	DRILLING MACHINE NO. B-2	LENGTH OF CASING 240
STATIC LEVEL 18	DRILLER Bill Jefferys	DISTANCE TO TOP OF SCREE
PUMPING LEVEL 120'	GRAVEL #2	TYPE SCREEN PVC
SPECIFIC CAPACITY 1	BAGS OF ~~CEMENT~~ Clay 15	SIZE OF SCREEN 6"
PUMPED WITH sub	DATE WELL COMPLETED 10/15/86	
DEPTH OF ~~CEMENT~~ GROUT Clay 0-220	DRILLER'S HELPER D. Pettit	
DEPTH GRAVEL PACKED 220-245		Wm. I. Jeffery

WELL DRILLER'S S
