Schlumberger

TEMPERATURE LOG

COMPANY DRILLERS INC.
WELL GRANT STREET TI
FIELD MELBOURNE
COUNTY BREVARD STATE FLORIDA

COUNTY	BREVARD
FIELD	MELBOURNE
LOCATION	
WELL	GRANT STREET TI
COMPANY	DRILLERS INC.

LOCATION: API SERIAL NO. / SECT. / TWP. / RANGE

Other Services: NONE

Elev.: PAD LEVEL / PAD LEVEL

Elev.: K.B. / D.F. / G.L.

Log Measured From: PAD LEVEL, 20.0 F above Perm. Datum

Drilling Measured From: K.B.

Date	16-MAY-88
Run Number	2
Depth Driller	2000.0 F
Depth Logger (Sent)	2000.0 F
Depth Logger	2000.0 F
Bottom Log Interval	2000.0 F
Top Log Interval	20.0 F
Casing-Driller	30 @ 0.000 F
Casing-Logger	
Bit Size	8 1/2
Type Fluid in Hole	GEL
Dens.	
Visc.	
pH	
Fluid Loss	
Source of Sample	NONE
Rm @ Meas. Temp.	
Rmf @ Meas. Temp.	
Rmc @ Meas. Temp.	
Source: Rmf / Rmc	
Rm @ BHT	
Rmf @ BHT	
Rmc @ BHT	
Max. Rec. Temp.	
Equipment Location	
Recorded By	
Witnessed By	

Run No.	1	2	
Bit No.	1		
Type Log	TEMP.		
Logger on Bottom	1:30		
Unit Number	0950		
Location			
Recorded By	RICHEL		
Witnessed By	EKAMP		

Run No.	2		
Service Order No.	825683		
Drilling Fluid Level	20.0 F		
Salinity	50.0 PPM		
Rmf @ BHT			
Rmc @ BHT			
Logging Speed	2000.0 F/HR		
Equipment Data			
Tool Number 1	HTS 778		
Tool Number 2	HTM 35		
Tool Number 3			
Tool Number 4			
Tool Number 5			
Tool Number 6			
Tool Number 7			
Tool Number 8			
Tool Number 9			
Tool Number 10			
Tool Number 11			
Tool Number 12			

FOLD HERE

The well name, location and borehole reference data were furnished by the customer.

All interpretations are opinions based on inferences from electrical or other measurements and we cannot, and do not guarantee the accuracy or correctness of any interpretations, and we shall not, except in the case of gross or wilful negligence on our part, be liable or responsible for any loss, costs, damages or expenses incurred or sustained by anyone resulting from any interpretations made by any of our officers, agents or employees. These interpretations are also subject to Clause 4 of our General Terms and Conditions as set out in our current Price Schedule.

REMARKS:

WELL CEMENTED 14-MAY-88
THANK YOU FOR USING SCHLUMBERGER!!!

PARAMETERS

NAME	VALUE	UNIT	NAME	VALUE	UNIT
BS	50.0000	IN	BHS	CASE	

SENSOR MEASURE POINT TO TOOL ZERO

TEMP	1.3	FEET	CCL	6.3	FEET
CVEL	0.0	FEET	TEMS	6.3	FEET
EXP	0.0	FEET			

-19.00	1.0000	-1.000	1.0000
CCL		DTEM(DF/F)	
0.0	100.00	70.000	90.000
TEMP(DEGF)		TEMP(DEGF)	

CP 27.772 FILE 3 16-MAY-88 08:20

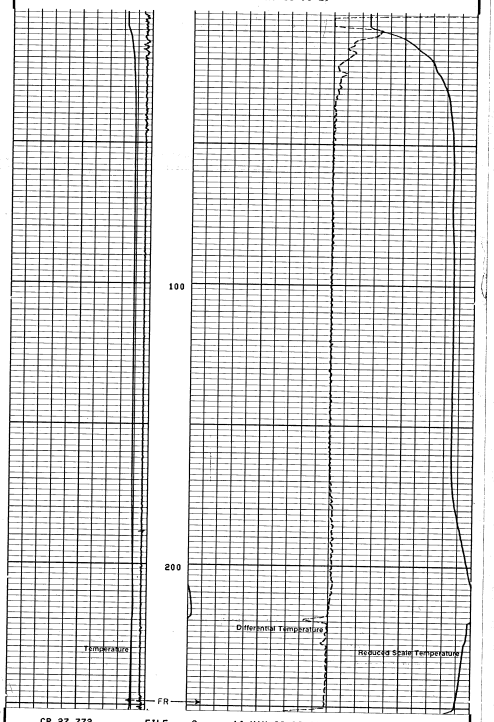

CP 27.772 FILE 3 16-MAY-88 08:30

-19.00	1.0000	-1.000	1.0000
CCL		DTEM(DF/F)	
0.0	100.00	70.000	90.000
TEMP(DEGF)		TEMP(DEGF)	

BEFORE SURVEY CALIBRATION SUMMARY

PERFORMED: 16-MAY-88 08:01
PROGRAM FILE: HTS (VERSION 27.772 85/08/07)

HTTA ELECTRONICS CALIBRATION SUMMARY

	MEASURED ZERO	MEASURED PLUS	CALIBRATED ZERO	CALIBRATED PLUS	UNITS
TEMP	38.1	230.6	32.0	212.0	DEGF

CP 27.772 FILE 0 16-MAY-88 08:01
